


DELAWARE STREET PROJECT UPDATE: 01/28/2020

With the work having already begun at the wharf by the City contractor Cirillo Brothers, the utility phase of the Delaware Street Project is set to begin on February 3rd. From Tuesday, January 28th until Friday, January 31st, Henkels and McCoy, the contractor for Delmarva, MSC, Comcast and Verizon will be doing preliminary work in order to prepare for the actual project to begin February 3rd; when they will begin saw cutting from 4th Street to The Strand. The saw cutting phase should take 5 days, with “No Parking” restrictions on various lengths of Delaware Street based on the daily progress made by the contractor.

You can follow project updates at www.newcastlecity.delaware.gov, or call the City office at 322-9812.

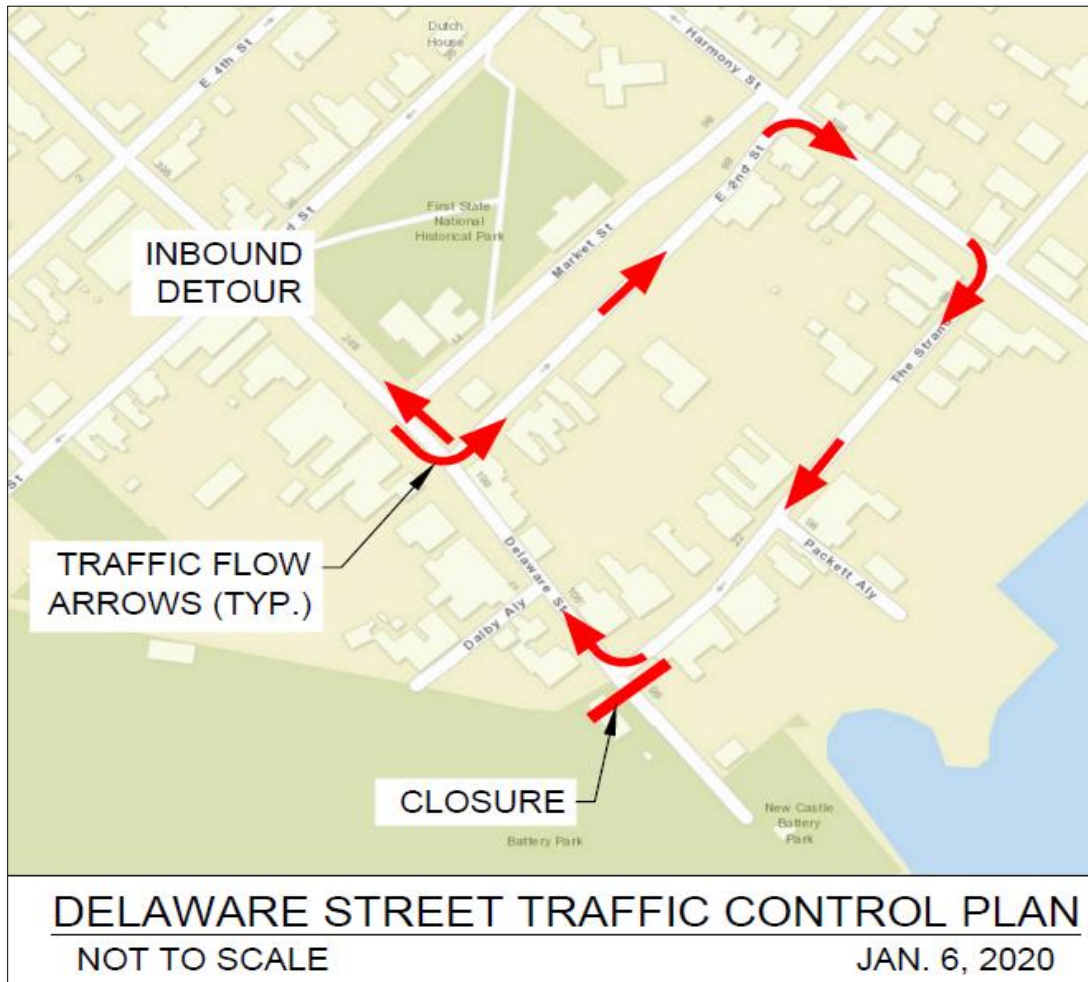

Delaware Street is closed from The Strand to the wharf during this phase of construction. The sidewalks will remain open for pedestrian use.

Cars will be detoured on Delaware Street from Second Street to Harmony to The Strand, with Delaware Street being one way from The Strand to Second Street.

This phase of construction is estimated to be approximately 6 weeks in duration.

Please contact the City office at 322-9801 with any questions or concerns.

We will provide updates as they become available.
